

*An Integral Service of*



# Ed's House Expansion Progress

March 21, 2024

# Suction and Oxygen Control Panel

The control panel is located directly opposite the clinical station.

The equipment and storage rooms for these systems have been built into our unfinished storage room in the lower level.







## Suites 6-10

Floors have been laid, bathroom tile will be finished today.

Overhead lifts to be installed in one day on Monday.


Plumbing fixtures will be installed on Tuesday.

We have begun to take delivery of some of our furniture, which is being stored until the rooms are complete.

Estimated completion is April 1 with occupancy by April 2.





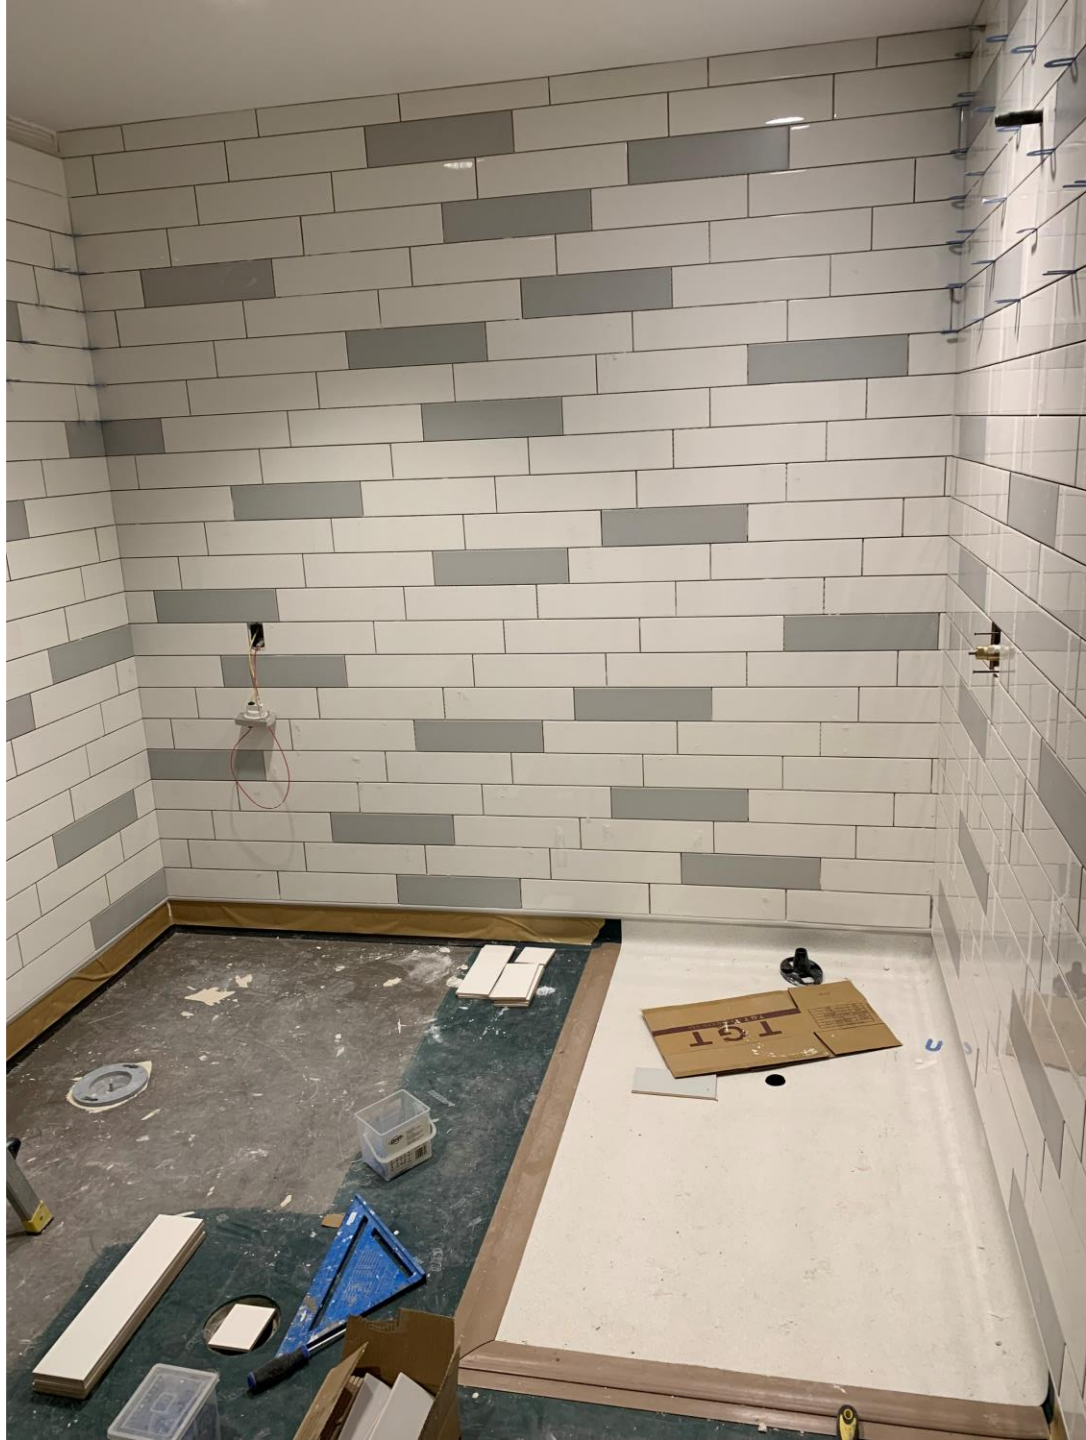

# Payment Progress

- An invoice is being created from CCN to the Foundation and February expenses totalling \$ 105,177 plus will be approved through Trish
- These are partial payments to BBA, Dalren, Holmes & Brakel, (suite furniture), Peterborough Appliance (suite fridges paid in full),TA Appliance (washer/dryer paid in full) and Class 1 Medical Gas Systems
- This will be completed end of month by our OA Carolyn until the expansion has been expensed
